

a **neighborly**™ company

Certificate of Completion

Overall Sealing Results

When we arrived,
YOUR DUCTS HAD:

288.7 CFM of Leakage, equivalent to a
54.5 Square Inch Hole


This equals 173.2 refrigerators full of air loss every hour.

After we finished,
YOUR DUCTS HAVE:

23.2 CFM of Leakage, equivalent to a
4.4 Square Inch Hole

This corresponds to a **92.0% Reduction** in
Duct Leakage.

Note: Duct Leakage results are calculated in Cubic Feet per Minute (CFM) measured at a standard OPERATING PRESSURE of 25 Pa.

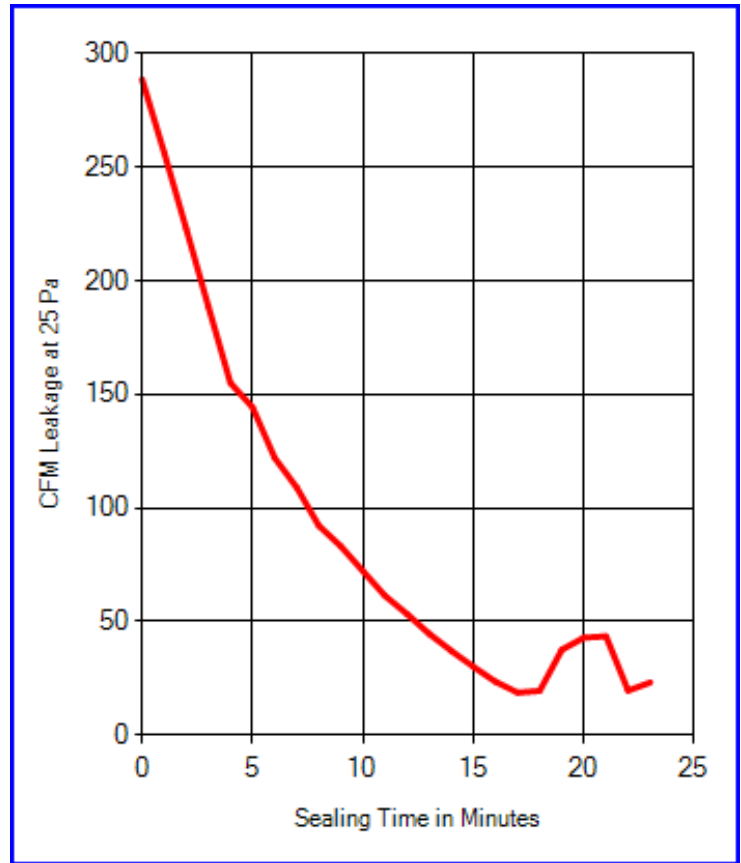

Duct Sealing Performed By:

Aire Serv
223 N Royal Ave
Front Royal, VA 22630 Phone: 540.631.9670

Aeroseal Technician **Oscar Solis**

Aeroseal Case ID **5202**

Date of Seal **11/20/2019**

System Description **Main Duct System**

Seal Description **Main Attic & Basement System**

Hardware **HomeSeal Connect**

AEROSEAL®
Duct Sealing From The Inside
